

MEMORANDUM

DATE: March 29, 2017


TO: Brian Dissette
Bill Hunter

FROM: Daniel A. Dombos II, P.E.

RE: SRF #5602-01-2a Monroe Boulevard & Indian Grove Lift Station Project Update

Current Progress:

Kalin Construction has been working to complete water infrastructure this week. Water main must pass pressure and bacteriological tests before going into service. Those tests are being conducted in phases as we work around the existing pipe. They have connected water services for the portion of the main that has completed and passed testing. Additional line stops have been placed to facilitate the completion of the water main between Beaver Court and Sheridan Road. While the water main work is wrapping up, the crew will complete the storm sewer and catch basin work.

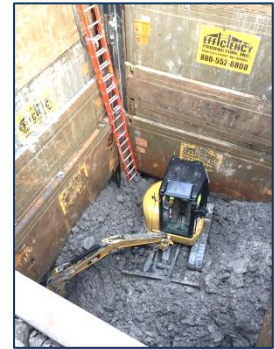

South of Lovejoy, sewer boring will take place mid- to late week. Work at the lift station continues. The picture on the right shows the mini excavator digging from within the caisson (approximately 20 feet below grade).

Construction Schedule:



In the coming week, water services off of the water main between Beaver Court and Sheridan road will be connected. Any remaining water connections will also be completed. Work on the lift station will continue. We anticipate beginning road reconstruction mid-April.

Weekly "tailgate talks" continue to take place on Thursdays at 9:30 a.m. for anyone with project-related questions or needs. Those meetings are held at the intersection of Monroe Boulevard and Lovejoy Avenue.
