

MEMORANDUM

DATE: April 19, 2017

TO: Brian Dissette
Bill Hunter

FROM: Daniel A. Dombos II, P.E.

RE: SRF #5602-01-2a Monroe Boulevard & Indian Grove Lift Station Project Update

Current Progress:

Roadway grading between Lovejoy and Aylworth is nearing completion in preparation for the reconstruction of the roadway, including curb and gutter and asphalt paving.

South of Lovejoy, Kalin continues making progress on the lift station and force main work. The valve vault for the lift station has been installed.




Construction Schedule:

Kalin will continue to work on the lift station and connecting sewers. A short stretch of storm sewer will be installed on Lovejoy Avenue.

Concrete work is tentatively scheduled to begin next week. Driveways will be inaccessible for approximately 4 days, and residents will be notified once the concrete has cured sufficiently to receive traffic. If you have any questions, please notify the crew or the Abonmarche inspector and they will advise you whether it will be necessary to stage a vehicle so you will be able to keep your schedule.

Once main line curbs are in place, the crew will create temporary gravel access ramps to allow residents to access their drives. Please keep an eye out for notices informing you of upcoming construction activities.

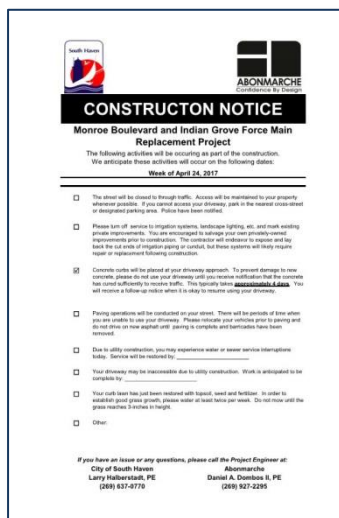

Weekly "tailgate talks" continue to take place on Thursdays at 9:30 a.m. for anyone with project-related questions or needs. Those meetings are held at the intersection of Monroe Boulevard and Lovejoy Avenue.
