

MEMORANDUM

DATE: April 26, 2017

TO: Brian Dissette

FROM: Corey A. Kandow, PE

RE: SRF #5602-01 North Shore Drive Project Update

North Shore Drive Project

Hooray...all municipal underground utility work (water, sanitary, and storm sewer) is complete for the entire North Shore Drive project.


Concrete sidewalk replacement has continued over the past week, and is approximately 95% complete in our Phase II (Dyckman to Brockway) section of the roadway. Sidewalk ramps still need to be placed, but can't be placed until the new curb and gutter is installed. As mentioned last week, several new trees have been planted recently. The remainder of our tree plantings will take place after our concrete sidewalks and curbs are complete.

Kent Power, Comcast and Frontier Communications have also continued the relocation of their facilities. Once complete, removal of the old existing utility poles will take place.

The schedule for the upcoming week includes road building operations (sand subbase and gravel base) on our Phase III (Brockway to Baseline) section of our roadway. Minor "final grading" of the gravel base in Phase II may also occur early in the week. Concrete crews are expected to be back onsite Wednesday, to start the new curb & gutter work.

Other than that, expect to see a continuation of utility relocation work by Kent Power, Comcast and Frontier. Traffic patterns should consistently improve as we head into the homestretch. With that being said, freshly placed concrete sidewalk and curb needs a full 3-4 days of cure time. Any vehicular traffic prior to that will result in broken/damaged concrete. Please stay off the newly placed concrete until the caution tape and flagging has been removed.

Finally, weekly on-site "tailgate talks" continue to take place for anyone with specific project related questions. These meetings take place on Wednesday's at 9:30 a.m. on the sidewalk in front of North Side Memories on Dyckman Avenue.

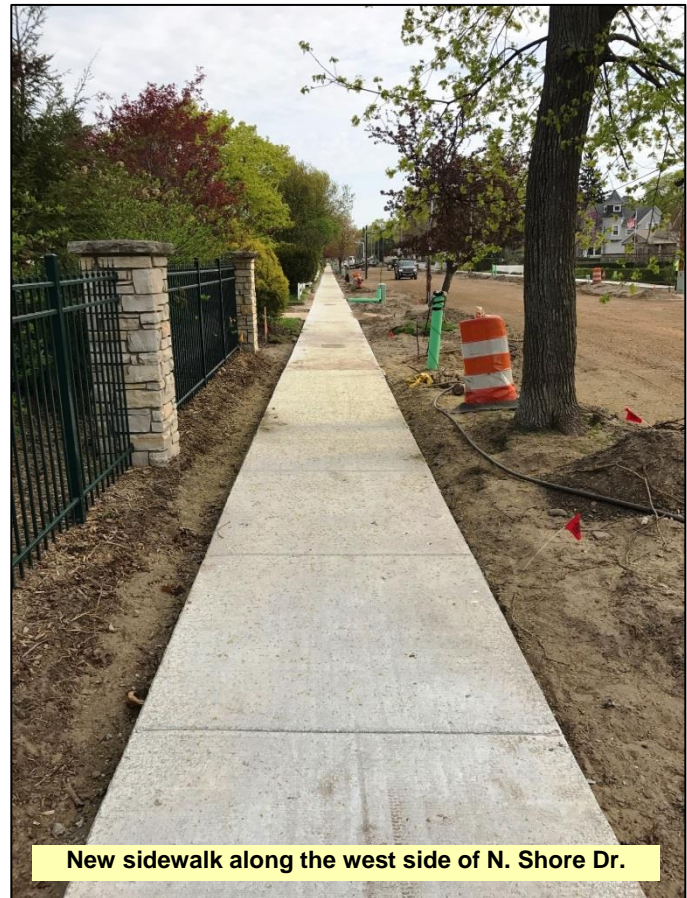

New sidewalk along the west side of N. Shore Dr.
