

MEMORANDUM

DATE: May 24, 2017

TO: Brian Dissette
Bill Hunter

FROM: Daniel A. Dombos II, P.E.

RE: SRF #5602-01-2a Monroe Boulevard & Indian Grove Lift Station Project Update

Current Progress:


Monroe Boulevard is continuing to take shape. Concrete sidewalks, drives and ramps are mostly poured. The first course of asphalt was placed last week and Kalin continues to work on topsoiling/turf restoration.

South of Lovejoy, Kalin successfully tested the new lift station last Friday.

The City's electrical department is working with their contractor to get electrical facilities onto new poles and get other utilities moved.



Construction Schedule:

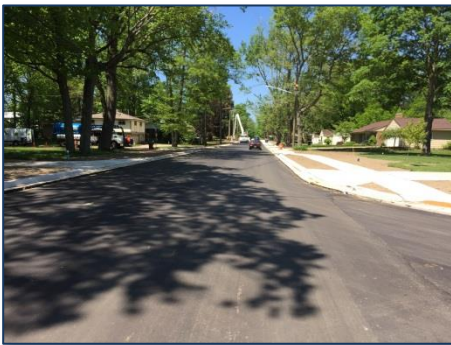

More asphalt is on the way at the end of this week. The contractor plans on installed the leveling course asphalt.

The lift station will go on line as soon as a new permanent electrical service has been installed. Following the switch to the new station, the old block structure will be demolished, an emergency standby generator will be installed. The crew will need to get back into Monroe Boulevard near the creek in order to complete gravity sewer rerouting. This was anticipated. At that point, work will be focused on landscape

plantings and signage prior to top course asphalt.

Weekly "tailgate talks" continue to take place on Thursdays at 9:30 a.m. for anyone with project-related questions or needs. Those meetings are held at the intersection of Monroe Boulevard and Lovejoy Avenue.
