

MEMORANDUM

DATE: June 28, 2017

TO: Brian Dissette
Bill Hunter


FROM: Daniel A. Dombos II, P.E.

RE: SRF #5602-01-2a Monroe Boulevard & Indian Grove Lift Station Project Update

Current Progress:

Signage and pavement markings have been installed on Monroe Boulevard. Major work on Monroe Boulevard will be drawing to a close this week. There will be walkthroughs and some cleanup work to come, but the heavy work is now behind us.

The Indian Grove Lift Station is on line and the site has been partially restored. The City is waiting for the gas service to set the generator and complete the work at that location.

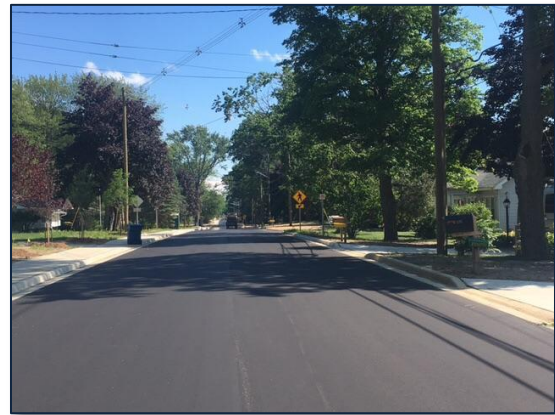

Construction Schedule:



The Lift Station's emergency standby generator will be installed as soon as the gas service is in place, and a concrete pad can be poured.

A landscaper has been hired by the City to plant the creek along the sewer easement to stabilize the banks and return them to a natural appearance.

Guardrail will be installed at the creek crossing as well.

Tomorrow's "tailgate talk" will be the final scheduled meeting. Those meetings are held at the intersection of Monroe Boulevard and Lovejoy Avenue. If a follow-up meeting is warranted, we will send a notification via the email list.
